

Sparked




Program Status Report
July 2025

Sparked Dashboard – July 2025

Operations Phase




Overall Status



Sparked Clinical Design Group

932

Members



~80 Regular attendees

Sparked Community Members

1,327



Downloads

1,200+



Followers

2,632

+57 in last 30 days



July


- 29-30 July – Sparked CDG & Community Co-Design Workshops (In-person; Sydney)



Sparked AU Core Technical Design Group

777

Members



~60 Regular attendees



Expert Hours

21,800+ hrs

Community Expert Time

Across 24 face-to-face events and 152 online meetings and webinars



August


- 8 – 12 August – MedInfo (Taipei)
- 11 – 14 August – National Allied Health Conference
- 18 – 20 August – HIC (Melbourne)
- 27 August – Sparked CDG Online



Sparked AU eRequesting Technical Design Group

651


Members



Sparked AU Patient Summary Project Team

281

Members



Published AUCDI R2

on 16 June 2025

September +

- 1-2 September – HL7AU Connectathon Tracks (In-person; Brisbane)
- 17 September – Sparked CDG Online
- 8 October – Sparked CDG Online
- Mid November – Sparked Event (In-person)
- 10 December – Sparked CDG Online
- December – HL7AU Connectathon TBC

Sparked Summary Status

Report Date:	28 July 2025	Program Status:	Green
Report Period:	July 2025	Program Phase:	Operations



Status Summary	Overall Health
<p>A new Financial Year has begun with work continuing to progress on all three FHIR Implementation Guides in preparation for ballot snapshots in August. Community engagement sessions have been key to reviewing draft content, offering feedback, and ensuring that specifications reflect real-world requirements.</p> <p>Another primary focus for July centers around our community engagement – this month in Sydney! The Sparked Clinical Design Group (CDG) and Community Co-Design Workshops are being held across 2 days (29-30 July). These are in-person events with the CDG focused on all things AUCDI R3 and the Community Co-Design Workshop looking at the detailed clinical and technical processes, as well as workflows for Chronic Condition Management.</p> <p>HL7 AU Connectathon preparations are also continuing. Sparked plans to run multiple tracks at the Connectathon in September which will include defining test scenarios, recruiting participants and finalising criteria, all designed to give implementers hands-on experience with specifications.</p>	Green

Milestone Summary				
Milestone			Status	
AUCDI R2 Published – June 2025			Completed	
Sparked Year 2 Complete – 30 June 2025			Completed	
Sparked CDG and Community Co-Design Workshops 29-30 July 2025			Green	
Schedule	Risks	Issues	Resources	Budget
Green	Green	Green	Green	Green

Program Engagement Status

Report Date:	28 July 2025	Program Status:	Green
Report Period:	July 2025	Program Phase:	Operations



Completed

June 25

- Stakeholder Engagement**
 - Clinical Colleges meetings
 - TDG meetings
- Events**
 - 3 June - Chronic Condition Management CFG Online Meeting
 - 24 June – Sparked Testing Event
- Communications**
 - Program Status Update
 - Emails to Community

Completed

July 25

- Stakeholder Engagement**
 - Clinical Colleges meetings
 - TDG meetings
- Events**
 - 29 & 30 July – In-person CDG & Co-design Meeting – Sydney
- Communications**
 - Program Status Update
 - Emails to Community

Planned

August 25

- Stakeholder Engagement**
 - Clinical Colleges meetings
 - TDG meetings
- Events**
 - 1-2 September – HL7AU Connectathon
 - Mid November – Sparked Event (In-person)
- Communications**
 - Program Status Update
 - Emails to Community


Product Status: AU Clinical Data for Interoperability (AUCDI)

Report Date:	28 July 2025
Report Period:	July 2025



Product Definition
Published data sets to be used as part of the AU Core FHIR standard (and other standards) for implementation across Australia spanning multiple use cases (AUCDI).

Dependencies		
Dependency	Due Date	Status
None identified		

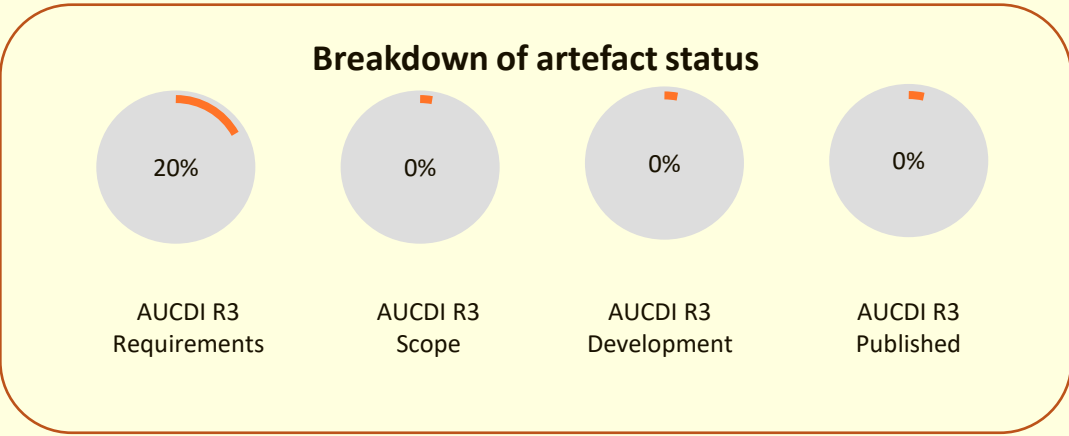

Product Phase
Planning

Overall Product Status		
Schedule	Risks	Issues
Green	Green	Green

Milestones Status		
Milestone	Due Date	Status
AUCDI R3 Requirements	Aug 2025	Green
AUCDI R3 Scope	Sep 2025	Green
AUCDI R3 Development	Jan 2026	NA
AUCDI R3 Draft for comment(s)	Feb 2026	NA
AUCDI R3 Published	Jun 2026	NA


Deliverable Status		
Deliverable	Due Date	Status
AUCDI R1 Published	Jul 2024	Complete
AUCDI R2 Published	Jun 2025	Complete
AUCDI R3 Published	Jun 2026	NA


NA: Not yet due to commence



Report Date:	28 July 2025
Report Period:	July 2025

Product Status: AU Core FHIR Implementation Guide


Product Definition		
AU Core sets the minimum expectations on FHIR resources to support conformance and implementation in systems for core clinical and administrative information.		
Dependencies		
Dependency	Due Date	Status
AUCDI R2 Published	Jun 2025	Complete
AU Base FHIR IG (5.x) Published 	Feb 2026	NA

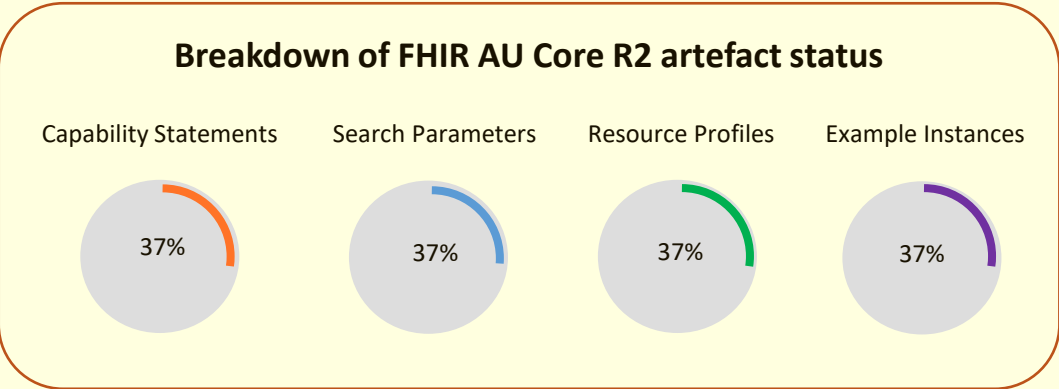

Product Phase	Overall Product Status		
Development	Schedule	Risks	Issues
	Green	Green	Green
Milestone Status			
Milestone	Due Date	Status	
AU Core FHIR IG R2 Development phase complete	Jul 2025	Green	
AU Core FHIR IG R2 Testing and Piloting of FHIR Standards phase complete	Dec 2025	NA	
AU Core FHIR IG R2 Ballot STU phase complete	Sep 2025	NA	
AU Core FHIR IG R2 Ballot Resolution phase complete	Dec 2025	NA	
Deliverable Status			
Deliverable	Due Date	Status	
AU Core FHIR IG R2 Draft for Testing and Piloting of FHIR Standards	Jul 2025	Green	
AU Core FHIR IG R2 Draft for Ballot	Aug 2025	NA	
AU Core FHIR IG R2 Published	Feb 2026	NA	


Product Status: AU Patient Summary FHIR Implementation Guide

Report Date:	28 July 2025
Report Period:	July 2025



Product Definition
AU Patient Summary sets the minimum expectations on FHIR resources to support conformance and implementation in systems for core clinical and administrative information for an Australian Patient Summary.

Dependencies		
Dependency	Due Date	Status
AUCDI R2 Published	Jun 2025	Complete
AU Base FHIR IF (5.x) Published HL7	Feb 2026	NA
AU Core R2 Published HL7	Feb 2026	NA

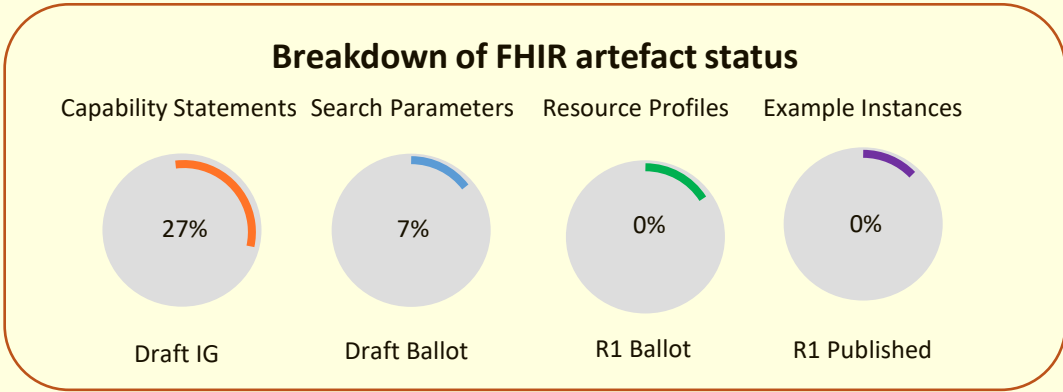

Product Phase	Overall Product Status		
Development	Schedule	Risks	Issues
	Green	Green	Green

Milestone Status		
Milestone	Due Date	Status
AU Patient Summary FHIR IG R1 Development phase complete	Jul 2025	Green
AU Patient Summary FHIR IG R1 Draft for Comment Ballot phase complete	Dec 2025	NA
AU Patient Summary FHIR IG R1 Testing and Piloting of FHIR Standards phase complete	Mar 2026	NA
AU Patient Summary FHIR IG R1 Ballot STU (WS) phase complete	Jun 2026	NA

Deliverable Status		
Deliverable	Due Date	Status
AU Patient Summary FHIR IG R1 Draft for Comment Ballot	Aug 2025	NA
AU Patient Summary FHIR IG R1 Draft for Testing and Piloting of FHIR Standards	Jul 2025	NA
AU Patient Summary FHIR IG R1 Draft for Ballot	Feb 2026	NA
AU Patient Summary FHIR IG R1 Published HL7	Jul 2026	NA



NA: Not yet due to commence




Report Date:	28 July 2025
Report Period:	July 2025

Product Status: AU eRequesting FHIR Implementation Guide

Product Definition
AU eRequesting sets the minimum expectations on FHIR resources to support conformance and implementation in systems for clinical service requesting.


Dependencies			
Dependency	Due Date	Status	
AU eRequesting Data for Interoperability (AUeReqDI) R1	Oct 2024	Complete	
AUCDI R2 Published	Jun 2025	Complete	
AU Base FHIR IG R6 Published	HL7 	Feb 2026	NA
AU Core FHIR IG R2 Published	HL7 	Feb 2026	NA

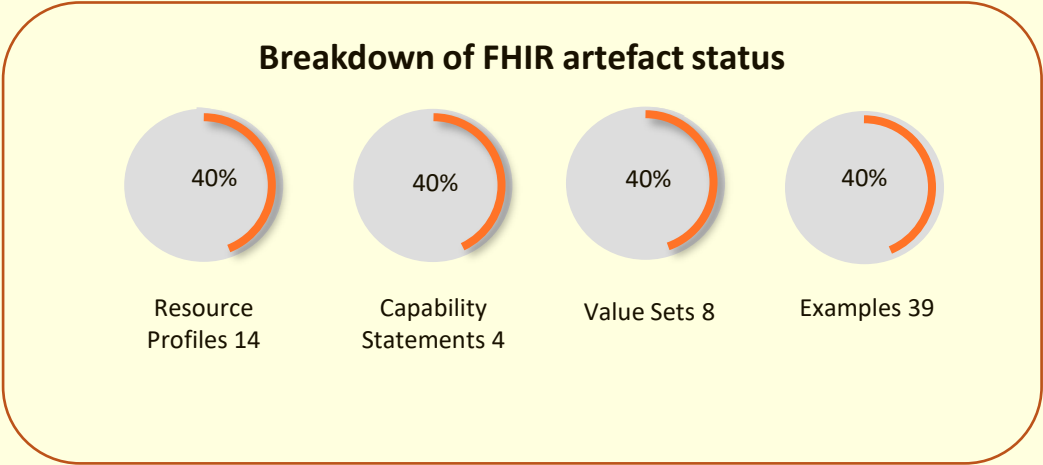

Product Phase
Development

Overall Product Status		
Schedule	Risks	Issues
Green	Green	Green

Milestone Status		
Milestone	Due Date	Status
AU eRequesting FHIR IG R1 Development phase complete	Jul 2025	Green
AU eRequesting FHIR IG R1 Testing and Piloting of FHIR Standards phase complete	Dec 2025	Green
AU eRequesting FHIR IG R1 Ballot STU phase complete	Sep 2025	NA
AU eRequesting FHIR IG R1 Ballot STU Resolution phase complete	Dec 2025	NA

Deliverable Status		
Deliverable	Due Date	Status
AU eRequesting FHIR IG R1 Draft for Testing and Piloting of FHIR Standards	Mar 2025	Completed
AU eRequesting FHIR IG R1 Draft for Ballot	Aug 2025	NA
AU eRequesting FHIR IG R1 Published	 Feb 2026	NA

Product Status: Terminology products FY25-26

Report Date:	28 July 2025
Report Period:	July 2025




Product Definition
Published SNOMED CT ValueSet/s to support the standardised, electronic requesting of, for example, Pathology and Radiology tests guided by the professional peak bodies.

Product Phase
Development

Overall Product Status		
Schedule	Risks	Issues
Green	Green	Green

Dependencies
Development of FHIR Terminology Target Operating Model (TOM)

Milestone Status		
Milestone	Due Date	Status
Define Statement of Work for Peak Bodies	Aug 2025	Green
Contract execution with Peak Bodies	Sept 2025	Green

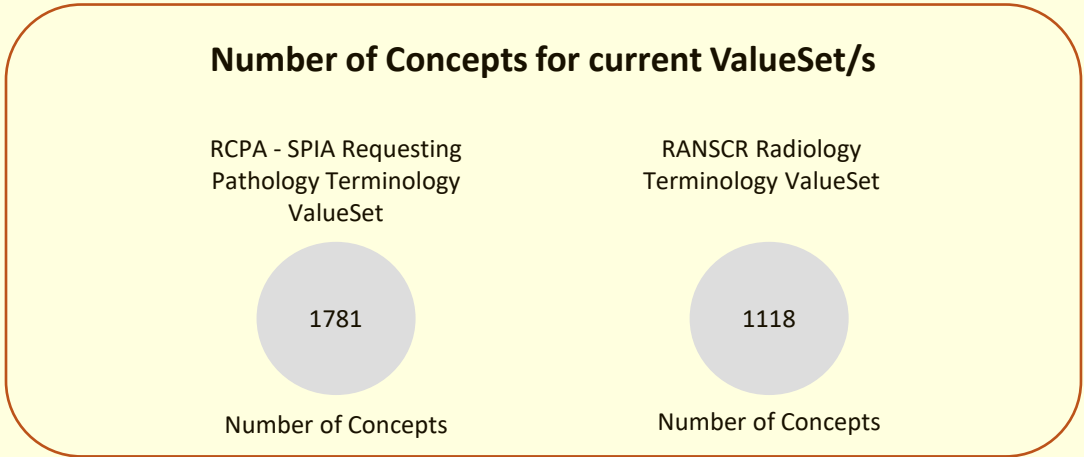

Deliverable Status		
Deliverable	Due Date	Status
Publication of FHIR Pathology Request ValueSet/s (R1)	Jun 2025	Complete
Publication of FHIR Radiology Request ValueSet/s (R1)	Jun 2025	Complete

Product Status: Sparked Testing Tools

Report Date:	28 July 2025
Report Period:	July 2025




Product Definition
Publicly available tools that test systems for their capability to conform to the AU FHIR Implementation Guides.

Product Phase
Operations

Overall Product Status		
Schedule	Risks	Issues
Green	Green	Green

Dependencies			
Dependency		Due Date	Status
AU eRequesting FHIR IG R1 Published	HL7	Feb 2026	NA
AU Core FHIR IG R2 Published	HL7	Feb 2026	NA
AU Patient Summary FHIR IG R1 Published	HL7	Jul 2026	NA

Milestone Status		
Milestone	Due Date	Status
AU Core R1 Inferno Test Kit Final Release	Mar 2025	Complete
AU Core R2 Inferno Test Kit First Release	Mar 2025	Complete
AU Patient Summary R1 Inferno Test Kit First Release	Mar 2025	Complete
AU Core R2 Sample FHIR Test Data	Nov 2025	NA
AU eRequesting R1 Sample FHIR Test Data	Jan 2026	NA
AU Patient Summary R1 Sample FHIR Test Data	Feb 2026	NA

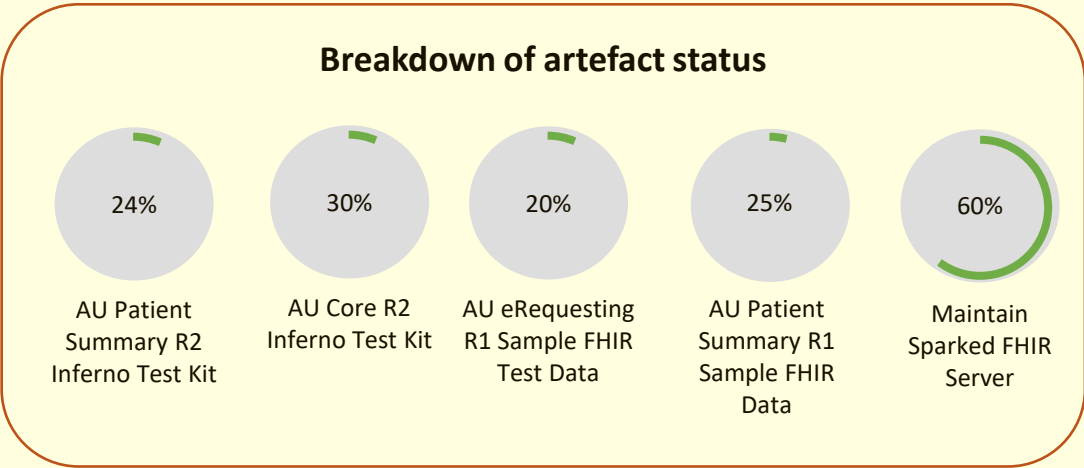

Deliverable Status		
Deliverable	Due Date	Status
AU Core R2 Inferno Test Kit Final Release	Mar 2026	NA
AU Patient Summary R1 inferno Test Kit Final Release	Aug 2026	NA

Product Status: Program Evaluation

Report Date:	28 July 2025
Report Period:	July 2025



Product Definition

An internal evaluation of the program effectiveness as well as enablers and barriers to implementation. Publications containing a guide that provides detailed information about the program components and supporting processes, approach, changes made, and lessons learnt.

Product Phase

Development

Overall Product Status		
Schedule	Risks	Issues
Green	Green	Green

Milestone Status		
Milestone	Due Date	Status
Baseline Data Collection	Jan 2024	Complete
Presentation of Plan and Prelim Results	May 2024	Complete
Sentiment Survey Distribution #1	Oct 2024	Complete
Post Improvement Analysis	Nov 2024	Complete
Sentiment Survey Distribution #2	May 2025	Complete

Deliverable Status		
Deliverable	Due Date	Status
Data Analysis and Synthesis	Apr 2024	Complete
Enhancement Plan Workshop	May 2024	Complete
Enhancement Action Plan	Nov 2024	Complete
Final Report	Apr 2025	Complete
Final Report – Sentiment 2 Survey	Aug 2025	Green

